Deloitte.



Burapahar and Baitarni West Coal Block
MIS Report dated 30-Sept-26


September 2026

Burapahar Coal Blocks

Deloitte.

High Level Schedule and Key Issues - Burapahar

Critical Task | Regular Task | Risk/Constraint | Key Milestones

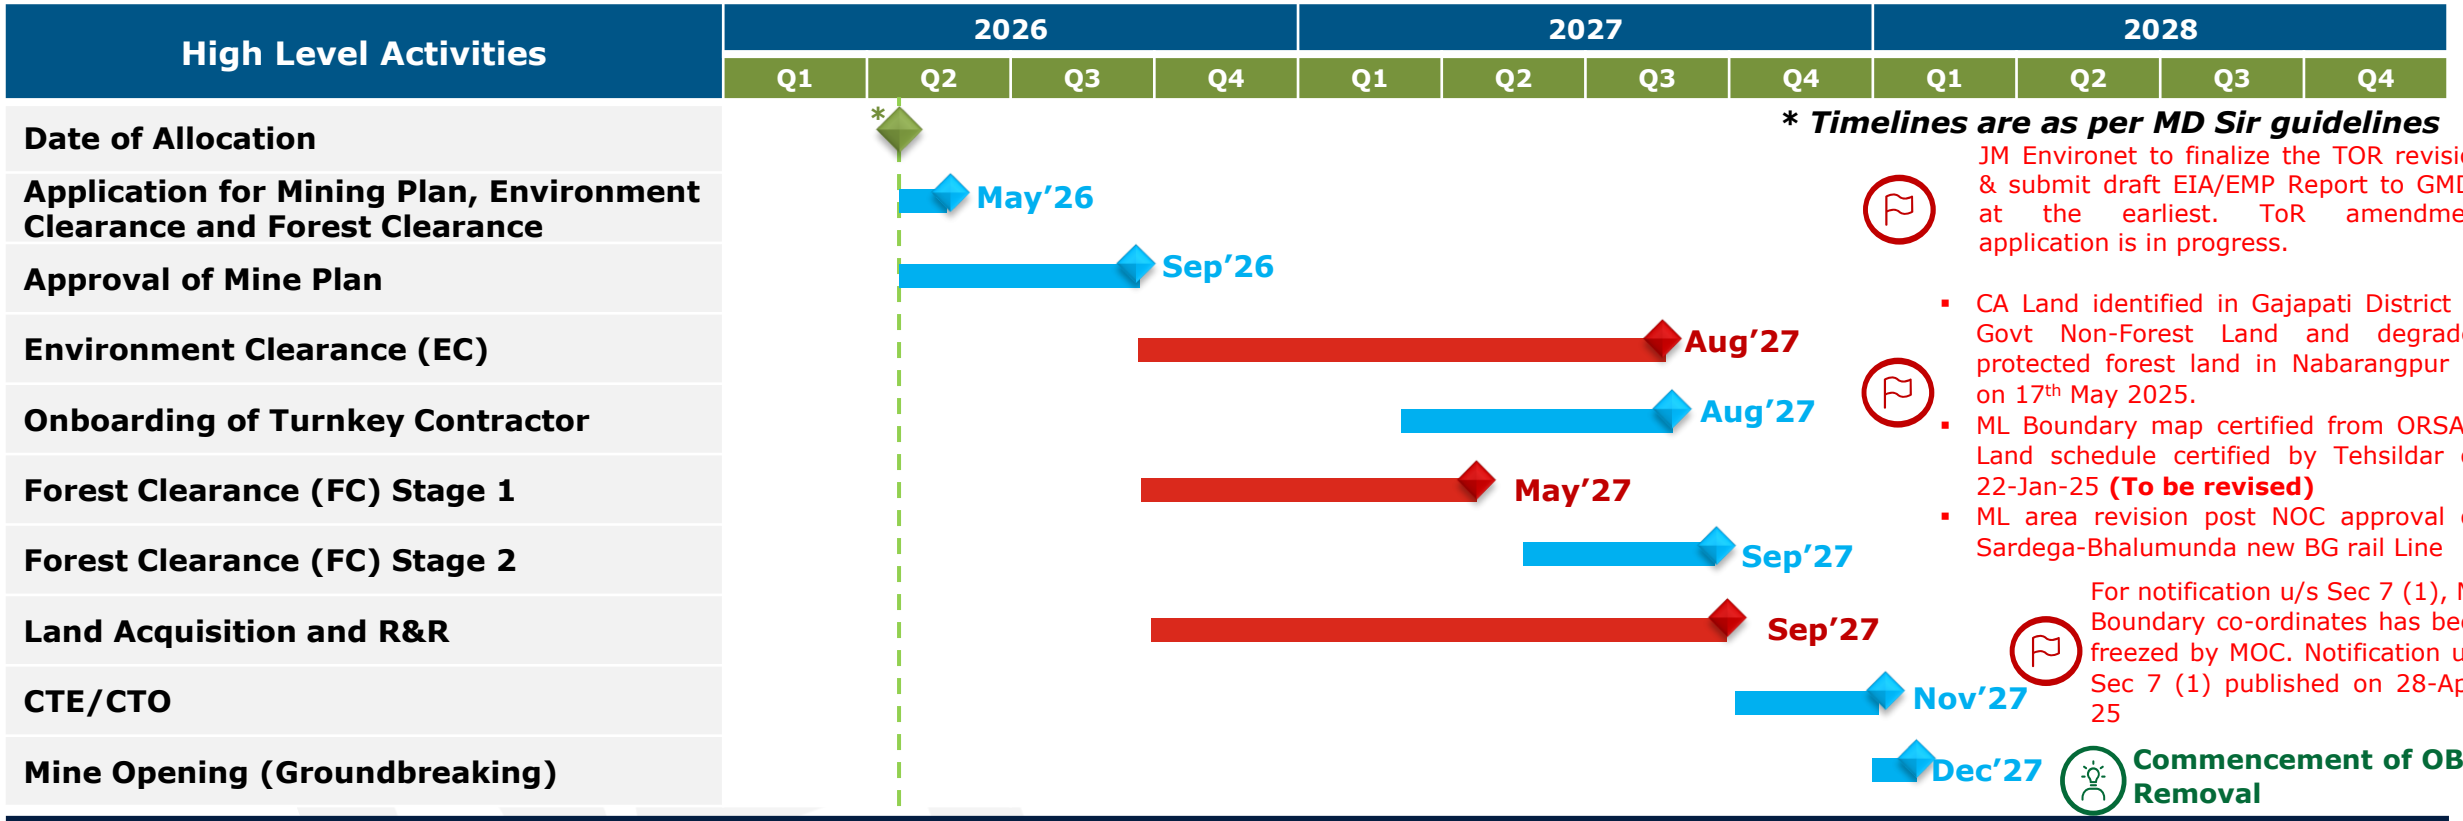

* ***Timelines are as per MD Sir guidelines***

JM Environet to finalize the TOR revision & submit draft EIA/EMP Report to GMDC at the earliest. ToR amendment application is in progress.

- CA Land identified in Gajapati District as Govt Non-Forest Land and degraded protected forest land in Nabarangpur as on 17th May 2025.
- ML Boundary map certified from ORSAC. Land schedule certified by Tehsildar on 22-Jan-25 **(To be revised)**
- ML area revision post NOC approval on Sardega-Bhalumunda new BG rail Line

For notification u/s Sec 7 (1), ML Boundary co-ordinates has been freezed by MOC. Notification u/s Sec 7 (1) published on 28-Apr-25

Commencement of OB Removal

Summary of Key Issues, Mitigation & Responsibility


Issues	Mitigation	Criticality	Action by	Due Date
Sec-9(1) publication	Land schedule has been finalized and submitted to BNB for certification of RI, Tehsildar.	Very High	BNB/GMDC	20-Oct-26
FDP Application by CEEP is pending.	All the documents are ready except the land schedule signed by Tehsildar. CEEP must expedite the process.	Very High	CEEP/GMDC	20-Oct-26

© 2026 Deloitte Touche Tohmatsu India LLP

*Corrigendum No. 2 issued on "**08-Apr-26 - Zero Date**" by MoC

High Level Schedule – Burapahar

Efficiency parameters comparison of Coal Block Development and Production Agreement (CBDPA) with Rev. CBDPA timelines and Actual/Forecast status

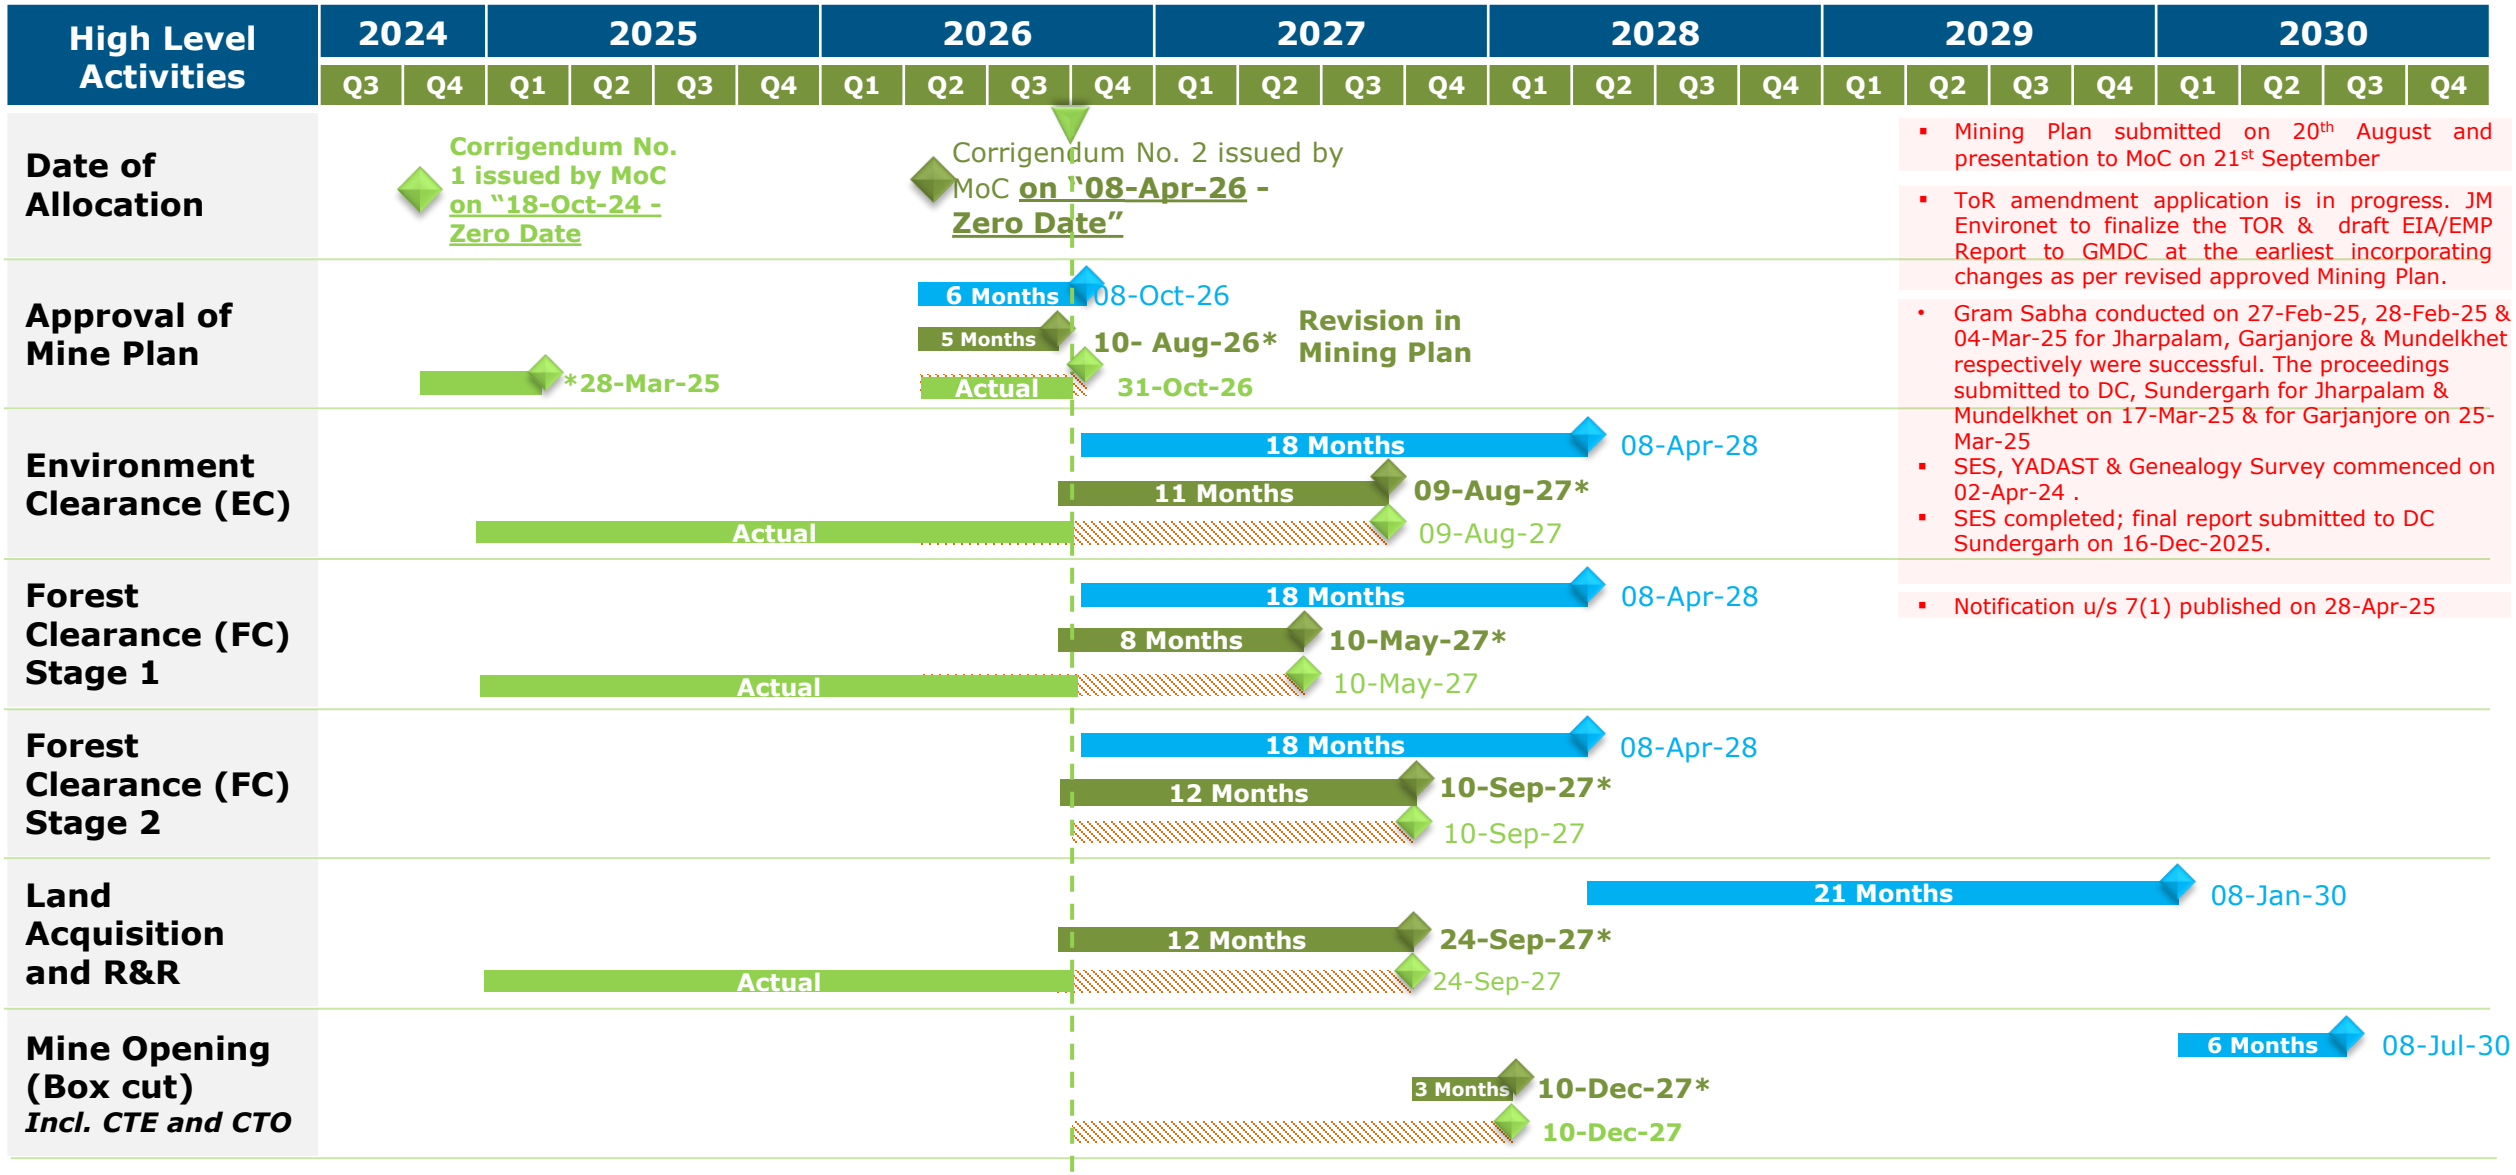

- Mining Plan submitted on 20th August and presentation to MoC on 21st September
- ToR amendment application is in progress. JM Environet to finalize the TOR & draft EIA/EMP Report to GMDC at the earliest incorporating changes as per revised approved Mining Plan.
- Gram Sabha conducted on 27-Feb-25, 28-Feb-25 & 04-Mar-25 for Jharpalam, Garjanjore & Mundelkhet respectively were successful. The proceedings submitted to DC, Sundergarh for Jharpalam & Mundelkhet on 17-Mar-25 & for Garjanjore on 25-Mar-25
- SES, YADAST & Genealogy Survey commenced on 02-Apr-24 .
- SES completed; final report submitted to DC Sundergarh on 16-Dec-2025.
- Notification u/s 7(1) published on 28-Apr-25

© 2026 Deloitte Touche Tohmatsu India LLP

Payment of the Upfront Amount

Burapahar

The upfront amount shall be payable in four equal installments [of 25% (twenty five percent each)]

Sr. No.	Installment	Upfront Amount in four equal installments of 25%	Payable To	Fully Explored Mines (Other than Schedule II)	Upfront Amount (INR)	Due Date as per CBDPA Timeline	Actual Payment Date	Remarks
1	First	25%	Nominated Authority	**Within 40 (forty) Business Days** of **execution of the Agreement i.e. 29-Mar-23**	**748,143,795**	**08-May-23**	**02-May-23**	**Payment Done**
2	Second	25%	State Government	**Within 15 (fifteen Business Days** of **execution of the Mining Lease or order by the Central Government** under Section 11 (1) of the CBA Act, 1957	**748,143,795**	**30-Dec-26***	**-**	**Revised timeline u/s 11(1)) as per ML boundary revision**
3	Third	25%	State Government	**Within 15 (fifteen Business Days** of **grant of the Coal Mine opening permission i.e. 7-Sep-27**	**748,143,795**	**22-Sep-27**	**-**	**-**
4	Fourth	25%	State Government	**Within 15 (fifteen Business Days** of **date of commencement of coal production**	**748,143,795**	**TBU**	**-**	**-**

© 2026 Deloitte Touche Tohmatsu India LLP


TBU - To be updated

Payment of the Performance Security

Burapahar

In case of delay in achievement of the Efficiency Parameters, there will be appropriation of Performance Security

Activity	% of Performance Security to be appropriated	Tentative Amount* (INR Cr)
Approval of Mining Plan	10%	53
FC and EC	10%	53
Land Acquisition and Possession of Land	25%	133
Mine Opening Permission	25%	133

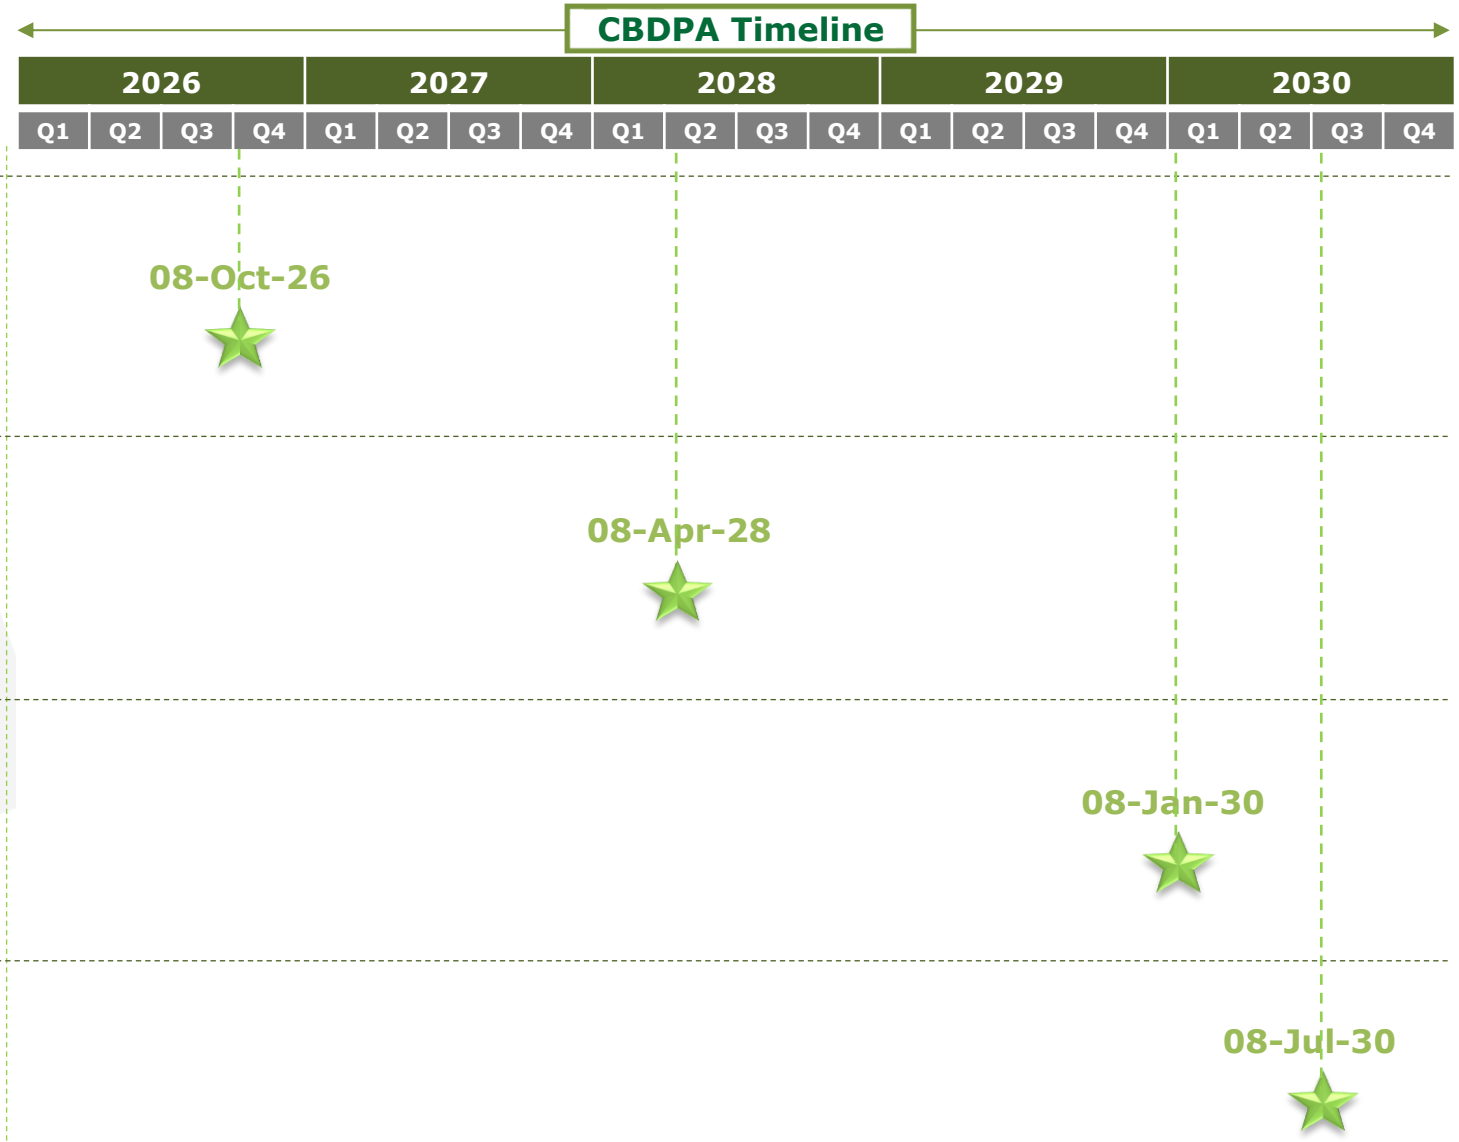

*Corrigendum No. 2 issued on "**08-Apr-26** - **Zero Date"** by MoC

* Amount will vary based on the Performance Security of the year

© 2026 Deloitte Touche Tohmatsu India LLP

Detailed Schedule Activities Mine Plan

Burapahar

Delayed In control Completed

Mining Plan as per CBDPA					
S. No.	**Milestone**	**Planned Finish**	**Exp/Act Finish**	**Status**	**Remarks**
1	Commencement of Work	15-Apr-26	15-Apr-26	●	Completed
2	Submission of Project Assumptions relating to Geology, Mine Design and Mine Planning Parameters and other considerations to GMDC management	25-Apr-26	25-Apr-26	●	
3	DGPS certified boundary map from ORSAC	20-May-26	25-Jun-26	●	Completed
4	Submission of Mine Plan to MoC	10-Aug-26	20-Aug-26	●	Completed
5	Presentation to MoC	20-Aug-26	21-Sep-26	●	Completed
6	Compliance to Observations by MoC	31-Aug-26	20-Sep-26	●	In Progress
7	Approval of Mine Plan from MoC	30-Sep-26	30-Oct-26	●	7-Oct-2026 is the timeline for MS-1

© 2026 Deloitte Touche Tohmatsu India LLP

Regular Task Key Milestones

*Corrigendum No. 2 issued on "**08-Apr-26 - Zero Date"** by MoC

Detailed Schedule Activities Turnkey Contractor

Burapahar

Delayed In control Completed

Onboarding of Turnkey Contractor for Coal and OB					
S. No.	**Milestone**	**Planned Finish**	**Exp/Act Finish**	**Status**	**Remarks**
1	Preparation and Floating of RFP	5-Oct-26	11-May-27		The tender will be floated tentatively after **revision of Mining Lease boundary & Approval of Revised Mining Plan.**
2	Pre-bid meeting and response to clarifications	29-Oct-26	1-Jun-27		
3	Submission of bids	20-Nov-26	25-Jun-27		
4	Evaluation of technical bids	4-Dec-26	12-Jul-27		
5	Evaluation of financial bids	28-Dec-26	6-Aug-27		
6	Obtaining approval from competent authority and award of work	11-Jan-27	27-Aug-27		
7	Performance security deposit	25-Feb-27	10-Sep-27		
8	Site handover	8-Mar-27	24-Sep-27		
9	Mobilization of resources of Bidder part	30-Mar-27	15-Oct-27		

*Corrigendum No. 2 issued on "**08-Apr-26 - Zero Date"** by MoC

© 2026 Deloitte Touche Tohmatsu India LLP

Detailed Schedule Activities EC

Burapahar

Delayed In control Completed

Environment Clearance						
S. No.	**Milestone**	**Planned Finish**	**Exp/Act Finish (C-0)**	**Exp/Act Finish (C-2)**	**Status**	**Remarks**
1	Start Date for Environmental Clearance Works	6-Oct-23	6-Oct-23 *(Completed)*	10-Sep-26		1. JM Environet to finalize the GMDC's proposal for Khurusalega Nallah diversion proposal which was shared on 18-Aug-24. 2. GMDC has provided comments on WLCP on 30-Sep-24 to JM Environet. **3. ToR amendment application is in progress. JM Environet to finalize the ToR & draft EIA/EMP Report to GMDC at the earliest incorporating changes subject to revised approved Mining Plan.** **4. Draft EIA & EMP report will be submitted to OSPCB.** **5. Fresh FDP application number for ToR amendment provided by CEEP.** **6. ToR amendment post modification of Mining Plan.**
2	M1 - Preparation of feasibility Report	1-Dec-23	22-Mar-24 *(Completed)*	01-Oct-26		
3	M2 - Submission of ToR Application (Ongoing)	4-Dec-23	23-Mar-24 *(Completed)*	05-Nov-26		
4	M3 - Grant of ToR by MoEF & CC	13-Mar-24	22-Jul-24 *(Completed)*	13-Jan-27		
5	M4 - Baseline Study & Data Collection	12-Dec-23	18-Jan-24 *(Completed)*	16-Oct-26		
6	M5 - Preparation of Additional Studies Reports	26-Jun-24	6-Oct-25	26-Apr-27		
7	M6 - Draft EIA submission to SPCB for PH	3-Apr-24	18-Jun-25	02-Feb-27		
8	M7 - Support in Public Hearing/ Public Hearing Ppt	22-May-24	6-Aug-25	22-Mar-27		
9	M8 - Final EIA to MoEF & CC	18-Jul-24	8-Oct-25	18-May-27		
10	M9 - Final Technical Presentation in front of EAC	15-Aug-24	11-Nov-25	15-Jun-27		
11	M10 - Grant of EC by MoEF & CC	18-Sep-24	21-Apr-26	09-Aug-27		

© 2026 Deloitte Touche Tohmatsu India LLP

Detailed Schedule Activities FC

Burapahar

Delayed In control Completed

Forest Clearance						
S. No.	**Milestone**	**Planned Finish**	**Exp/Act Finish (C-0)**	**Exp/Act Finish (C-2)**	**Status**	**Remarks**
1	Start Date for Forest Clearance Works	6-Oct-23	6-Oct-23 (Completed)	10-Sep-26	●	**1. CA Land identified in Gajapati District as Govt Non-Forest Land and degraded protected forest land in Nabarangpur as on 17th May 2025.** **2. Tree Enumeration completed.** 3. Letter has been issued to ORSAC to facilitate CEEP for DGPS survey of CA Land on 27-Mar-25. 4. CEEP generated FDP file number on 13-May-25 and provided the same to JM Environment for ToR amendment. **5. Close follow up being carried out with CEEP team for early filing of FDP.**
2	M1 - Project & Forest Area mapped, Land Details	18-Dec-23	27-Jan-25 (Completed)	18-Sep-26	●	
3	M2 – DGPS field survey by ORSAC with CMPDIL/Revenue/Forest Dept.	2-Jan-24	29-Jan-24 (Completed)	30-Sep-26	●	
4	M3 - CA Land Process	22-Apr-24	04-Jun-25	15-Oct-26	●	
5	M4 - Activities for Tree Enumeration	2-Feb-24	14-Jan-25 (Completed)	30-Oct-26	●	
6	M5 - Online filing of Draft FDP & Final FDP	13-Feb-24 & 2-May-24	19-Jun-25	13-Nov-26 & 02-Jan-27	●	
7	M6 - Activities for approval under FRA 2006	31-Oct-24	4-Jun-26	30-Jun-27	●	
8	M7 - NOC Gram Panchayat, Arch. Dept.,& DC	15-Oct-24	15-May-26	15-Jun-27	●	
9	M8 - Details of land & R&R required for FC Appl.	29-May-24	5-Jan-26	29-Jan-27	●	
10	M9 - Processing by the Nodal Officer of the Processing Authority	28-Mar-24	3-Jul-25	28-Dec-26	●	
11	M10 - Processing of the proposal by the DFOs/ DCs	13-May-24	18-Aug-25	13-Jan-27	●	
12	M11 - Processing of the proposal by the CF/CCF	6-Jun-24	15-Sep-25	6-Feb-27	●	
13	M12 - Processing of the proposal by the Nodal Officer	1-Jul-24	28-Jan-26	1-Mar-27	●	
14	M13 - Issuance of Stage-I FC	12-Aug-24	13-Mar-26	12-Apr-27	●	
15	M14 - SSWLP Formulation and submission	27-Aug-24	27-Mar-26	27-Apr-27	●	
16	M15 - Payment for NPV, CA Land etc.	10-Sep-24	13-Apr-26	27-May-27	●	
17	M16 - Compliance activities of Stage-I conditions	3-Oct-24	6-May-26	15-Jul-27	●	
18	M17 - Issuance of Stage-II FC	27-Nov-24	29-Jun-26	10-Sep-27	●	

Ongoing

Ongoing


© 2026 Deloitte Touche Tohmatsu India LLP

Detailed Schedule Activities – Land Acquisition and R&R


Burapahar

Land

Government Land(Ha)

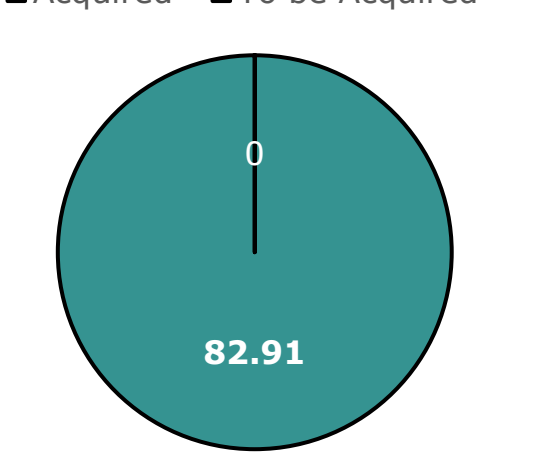


Private Land(Ha)

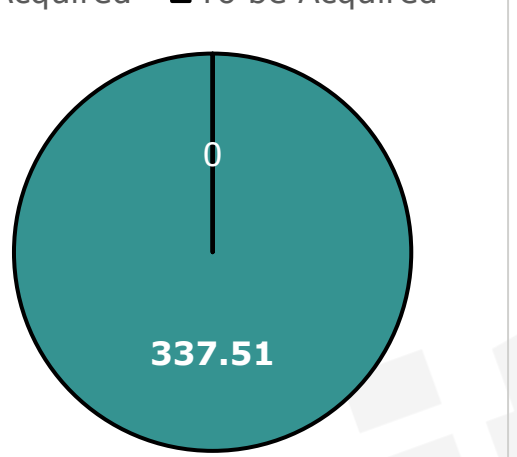

PAP

Project Impact

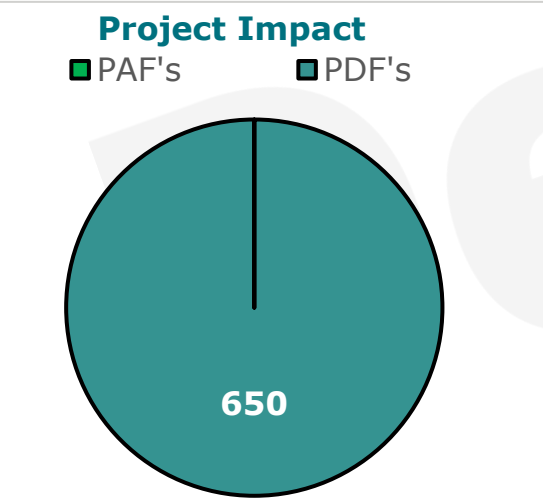

PAF's Detail

- Cash in Liew of Land
- Employment in Lieu of Land

Land Acquisition				
*Forest Land =186 Ha	*Govt. Land = 82.91 Ha	*Private Land = 337.51 Ha		
S. No.	**Milestone**	**Planned Finish (C-0)**	**Exp/Act Finish (C-0,1)**	**Exp/Act Finish (C-2)**
1	M1 - Preparation of Land documents for filling of land acquisition	08-Jan-24	**22-Jan-25**	12-Jun-26
2	M2 - Notification in Official Gazette under Section 4(1)	08-Feb-24	**13-Mar-24**	***13-Mar-24**
3	M3 - Notification u/s 7(1) of CBA (A&D) Act, 1957	11-Mar-24	**28-Apr-25**	28-May-26
4	M4 - Socio Economic Survey	3-May-24	**16-Dec-25**	***16-Dec-25**
5	M5 - Section 8 hearing and disposal of objections	26-Apr-24	**27-Jun-25**	***27-Jun-25**
6	M6 - Notification u/s 9(1) of CBA (A&D) Act, 1957-Declaration of Acquisition. Current Status	16-May-24	3-Dec-25	15-Oct-26
7	M7 - Notification u/s 11(1) of CBA (A&D) Act, 1957	31-May-24	23-Dec-25	30-Nov-26

Resettlement & Rehabilitation			
S. No.	**Milestone**	**Planned Finish (C-0)**	**Exp/Act Finish (C-2)**
1	M8 - Determine and Finalize Compensation u/s 13 and 14 of CBA (A&D) Act, 1957	04-Jul-24	
2	M9 - R&R Scheme and Compensation Scheme award	03-Jul-24	
3	M10 - Compensation Payment	07-Aug-24	
4	M11 - Transfer & physical possession of Private Land (for at least 5 years of operation)	15-Nov-24	
5	M12 - Transfer & physical possession of balance Private Land	06-Dec-24	

© 2026 Deloitte Touche Tohmatsu India LLP

***Land Breakup to be updated post Land Schedule finalization subject to ML area revision.**

***Earlier notification is valid post Corrigendum-2**

Actions to be taken within next 15 days

Burapahar

Delayed | In control | Completed

Particulars	Contractor	Status as on date	Criticality	Action Plan
Mining Plan		▪ ML Boundary certification from ORSAC received on 25-Jun-26. ▪ Mining Plan submitted to MOC on 20-Aug-26. ▪ Review & compliance completed and presented to MoC on 21st September 2026.		**Note: October 8 is the last date for MS-01 as per CBDPA.**
Land Acquisition and R&R	BNB	▪ Gramsabha conducted successfully. The proceedings submitted to DC, Sundergarh for Jharpalam & Mundelkhet on 17-Mar-25 & for Garjanjore on 25-Mar-25. ▪ SES, Yadast & Genealogy Survey commenced on 02-Apr-25. and 1078 families completed as on 30th Jun. SES completed; final report submitted on 09-Dec-25. ▪ Notification u/s 7(1) published on 28-Apr-25. Notification u/s 8 (2) published by MoC on 27-Jun-25. ▪ Corrigendum-2 issued on 08-Apr-26 by MoC. ▪ ML Boundary certification from ORSAC received on 25-Jun-26. ▪ **Land Schedule Finalized and received from BNB on 23-Jul-26**		▪ **CBA Sec-9(1) to be published .** ▪ **Land Schedule from BNB received on 23-Jul-2026 and review by GMDC is in progress.** ▪ **YADAST is under progress.**
EC	JM Environet	▪ ToR approved on 22-Jul-24. ▪ All the baseline studies and additional studies field work has been completed. ▪ **The draft EIA & EMP report has been shared by JM Environet on 17-Aug-24.**		▪ **The review of the 1st draft report is being done by GMDC.** ▪ **Draft EIA and EMP report should be submitted at the earliest with ToR modification post revised Mining Plan approval.**

Actions to be taken within next 15 days

Burapahar

Delayed In control Completed

Particulars	Agency	Status as on date	Criticality	Action Plan
FC	CEEP	▪ **Regarding identification of CA Land; Letter has been sent to DFO on 27-Jun-24 regarding identification of CA Land at Gajapati.** ▪ Tehsildar, Nuagada, Gajapati has sent letter to all RI's for allotment of non-forest CA land on 13-Aug-24. ▪ RI of Keredango submitted the trace map and land schedule to Nuagada Tehsildar on 23-Aug-2024. ▪ **Nuagada Tehsildar sent the file to ADM Gajapati on 03-Oct-24** for allotment of CA land. ▪ DC, Gajapati sent letter to DFO Paralakhemundei on 4-Nov-24 to offer views on allotment of CA land. ▪ DFO, Paralakhemundi has sent letter to DC, Gajapati on 09-Dec-24, confirming that the land identified for CA land is falling inside Keradanga UDPF (Un-demarcated Protected Forest) and is only suitable for Additional compensatory Afforestation. Letter received from DFO to DC Gajapati on 16-Dec-24 requesting to identify another 186 Ha of land adjacent to the land identified. ▪ **CA Land identified & allotted.** ▪ **Letter for DGPS survey of CA land submitted to ORSAC on 07-May-26.** ▪ **Demand from ORSAC received on 12-Jun -2026.**		▪ **All pre-requisites for FDP application is to be kept ready before approval of revised mining plan.** ▪ **DGPS survey of CA land to be completed at the earliest.**

Draft

Actions to be taken within next 15 days

Burapahar

Delayed In control Completed

Particulars	Agency	Status as on date	Criticality	Action Plan
Logistics	IPRCL	▪ DPR report for road diversion completed and submitted on 20-Dec-24. ▪ Bhalumunda to Sardega Rail corridor has been approved by Cabinet meeting dated 27-Aug-24. ▪ Survey & Geotechnical work for existing road diversion has been completed on 25-Nov-2024. ▪ FSR submitted to GMDC for review on 09-Apr-25. ▪ SECR (IR) requested NOC for land acquisition inside Mining block that falls in Sardega-Bhalumunda Railway Line. ▪ GMDC has agreed to NOC on meeting conducted by MoC with MoR ▪ Letter sent to SECR on 12-Aug-25 seeking land details to expediate NOC. SECR shared details on 18-Sep-25. ▪ ML boundary revised to 594.6 Ha post Corrigendum-2		▪ IPRCL will share the timeline for DPR preparation after approval from GMDC. ▪ A letter to be conveyed to SERL for proposed Sardega-Bhalumunda rail alignment change as it is superimposing 19.2 Acre of land inside ML area. ▪ Letter sent to LAO, Hemgir with enclosed verified land details to be acquired by IR for Sardega-Bhaluminda project. ▪ Response letter sent to SECR post validation on 14-Oct-25 for boundary co-ordinate validation and GMDC will approach MOC for ML Boundary revision. Follow-up emails shared & awaiting response from SECR ▪ FSR to be submitted post revision of Mining Plan Approval


Deloitte

High Level Schedule of IPRCL

Burapahar

Consultancy Services of Pre-Feasibility study report for the logistics of movement of coal from Burapahar Coal Block of GMDC

Delay | Key Milestones | Plan | Actual | Forecast

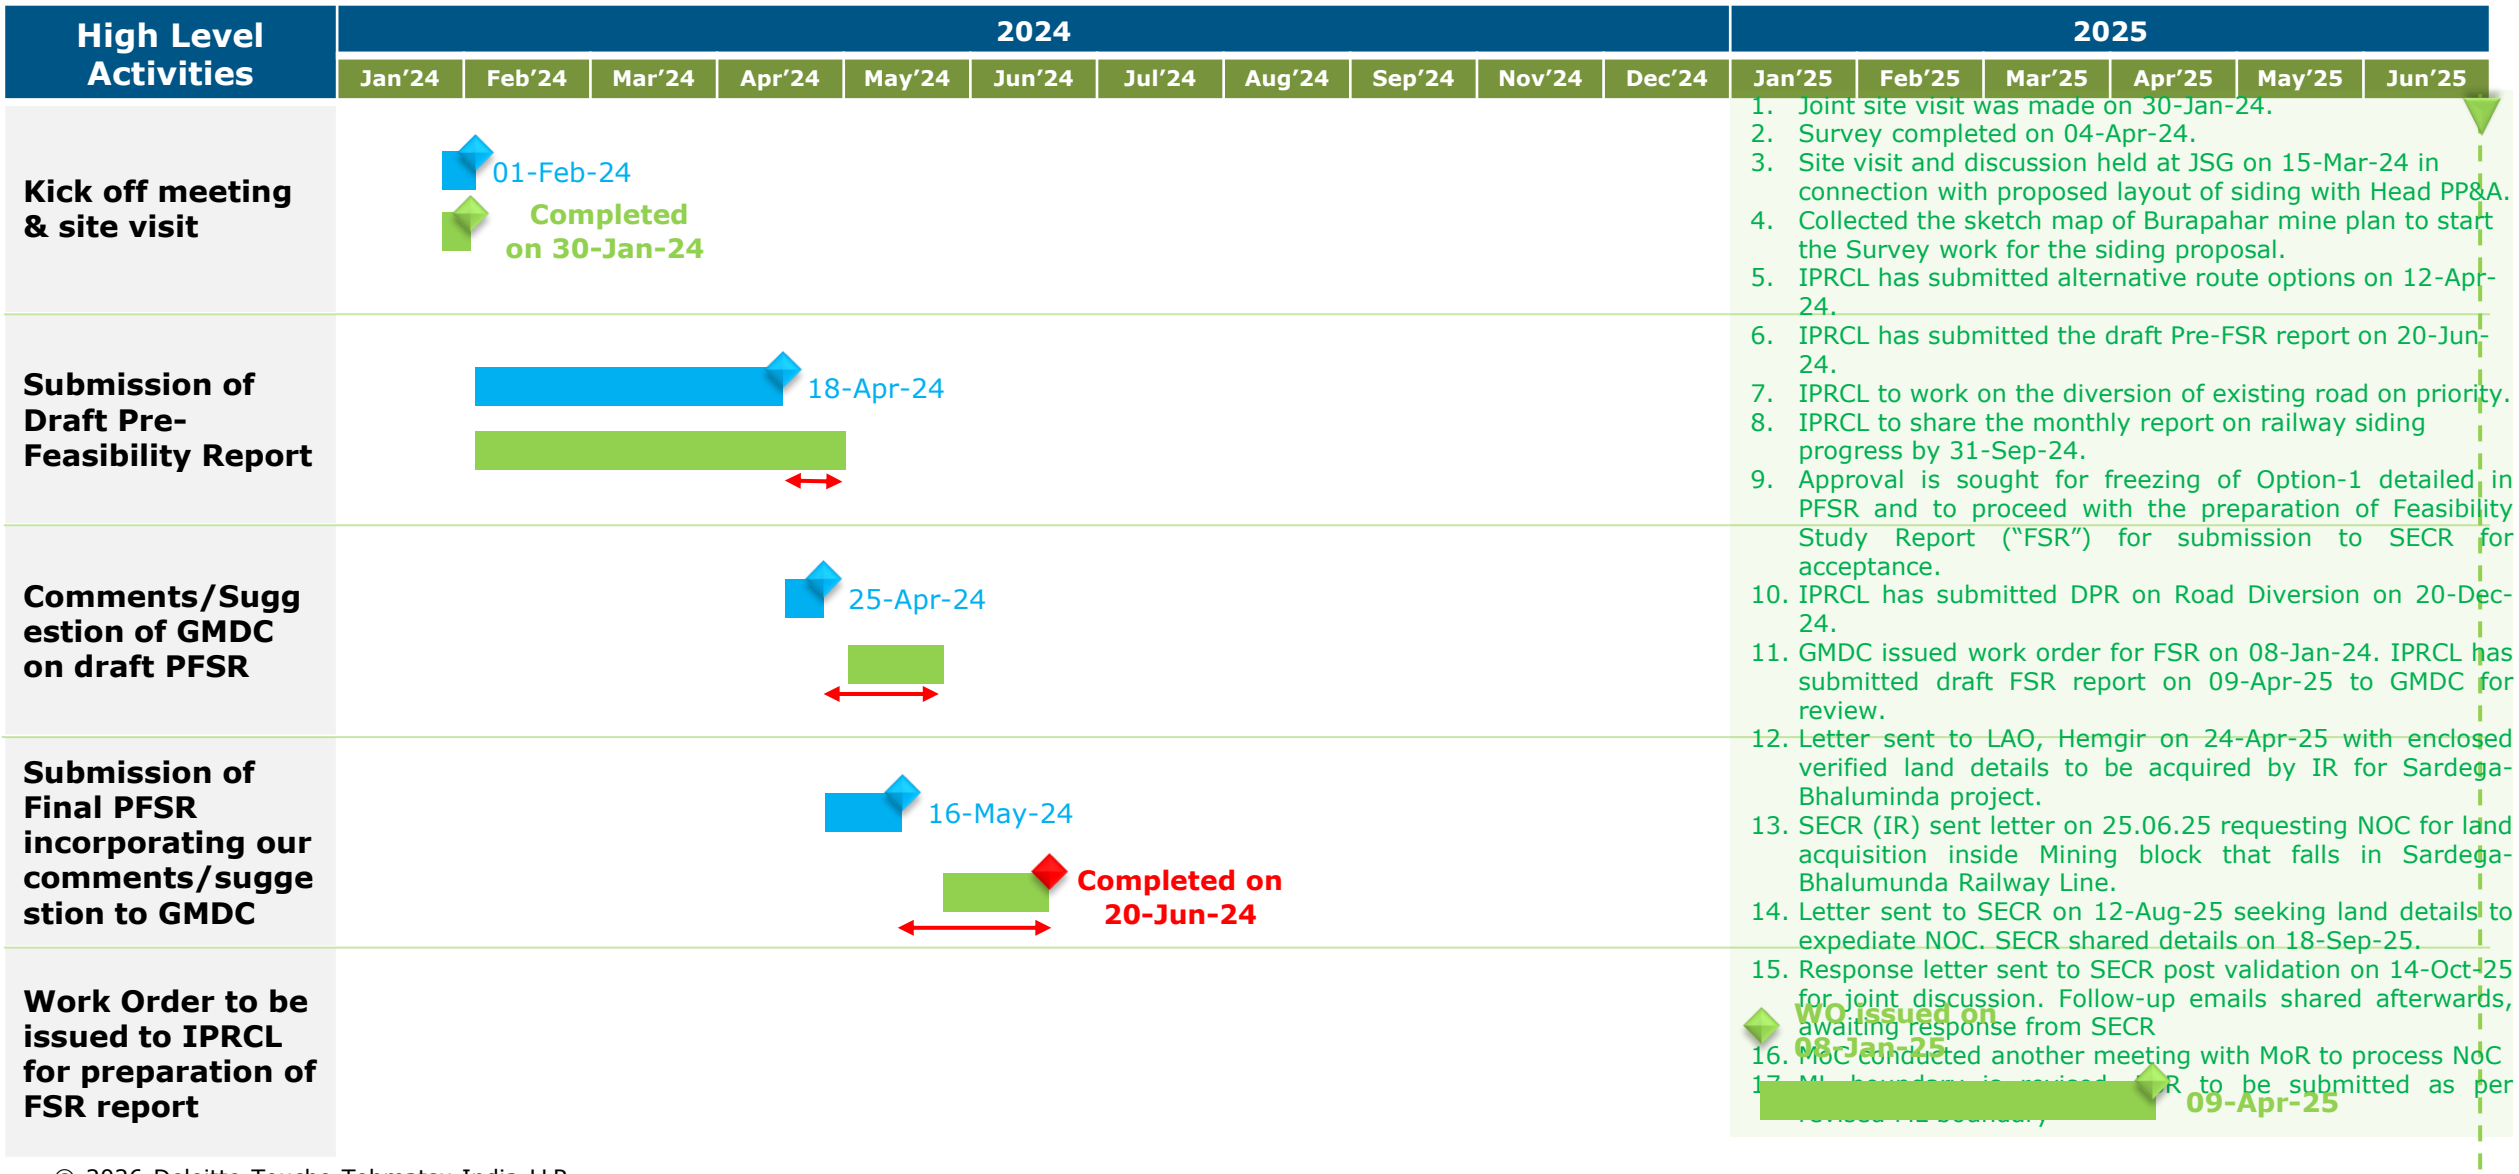


1. Joint site visit was made on 30-Jan-24.
2. Survey completed on 04-Apr-24.
3. Site visit and discussion held at JSG on 15-Mar-24 in connection with proposed layout of siding with Head PP&A.
4. Collected the sketch map of Burapahar mine plan to start the Survey work for the siding proposal.
5. IPRCL has submitted alternative route options on 12-Apr-24.
6. IPRCL has submitted the draft Pre-FSR report on 20-Jun-24.
7. IPRCL to work on the diversion of existing road on priority.
8. IPRCL to share the monthly report on railway siding progress by 31-Sep-24.
9. Approval is sought for freezing of Option-1 detailed in PFSR and to proceed with the preparation of Feasibility Study Report ("FSR") for submission to SECR for acceptance.
10. IPRCL has submitted DPR on Road Diversion on 20-Dec-24.
11. GMDC issued work order for FSR on 08-Jan-24. IPRCL has submitted draft FSR report on 09-Apr-25 to GMDC for review.
12. Letter sent to LAO, Hemgir on 24-Apr-25 with enclosed verified land details to be acquired by IR for Sardega-Bhaluminda project.
13. SECR (IR) sent letter on 25.06.25 requesting NOC for land acquisition inside Mining block that falls in Sardega-Bhalumunda Railway Line.
14. Letter sent to SECR on 12-Aug-25 seeking land details to expediate NOC. SECR shared details on 18-Sep-25.
15. Response letter sent to SECR post validation on 14-Oct-25 for joint discussion. Follow-up emails shared afterwards, awaiting response from SECR
16. MoC conducted another meeting with MoR to process NoC
17. ML boundary is revised, FSR to be submitted as per revised ML boundary

© 2026 Deloitte Touche Tohmatsu India LLP

Baitarni West Coal Blocks

Deloitte.

High Level Schedule and Key Issues – Baitarni West

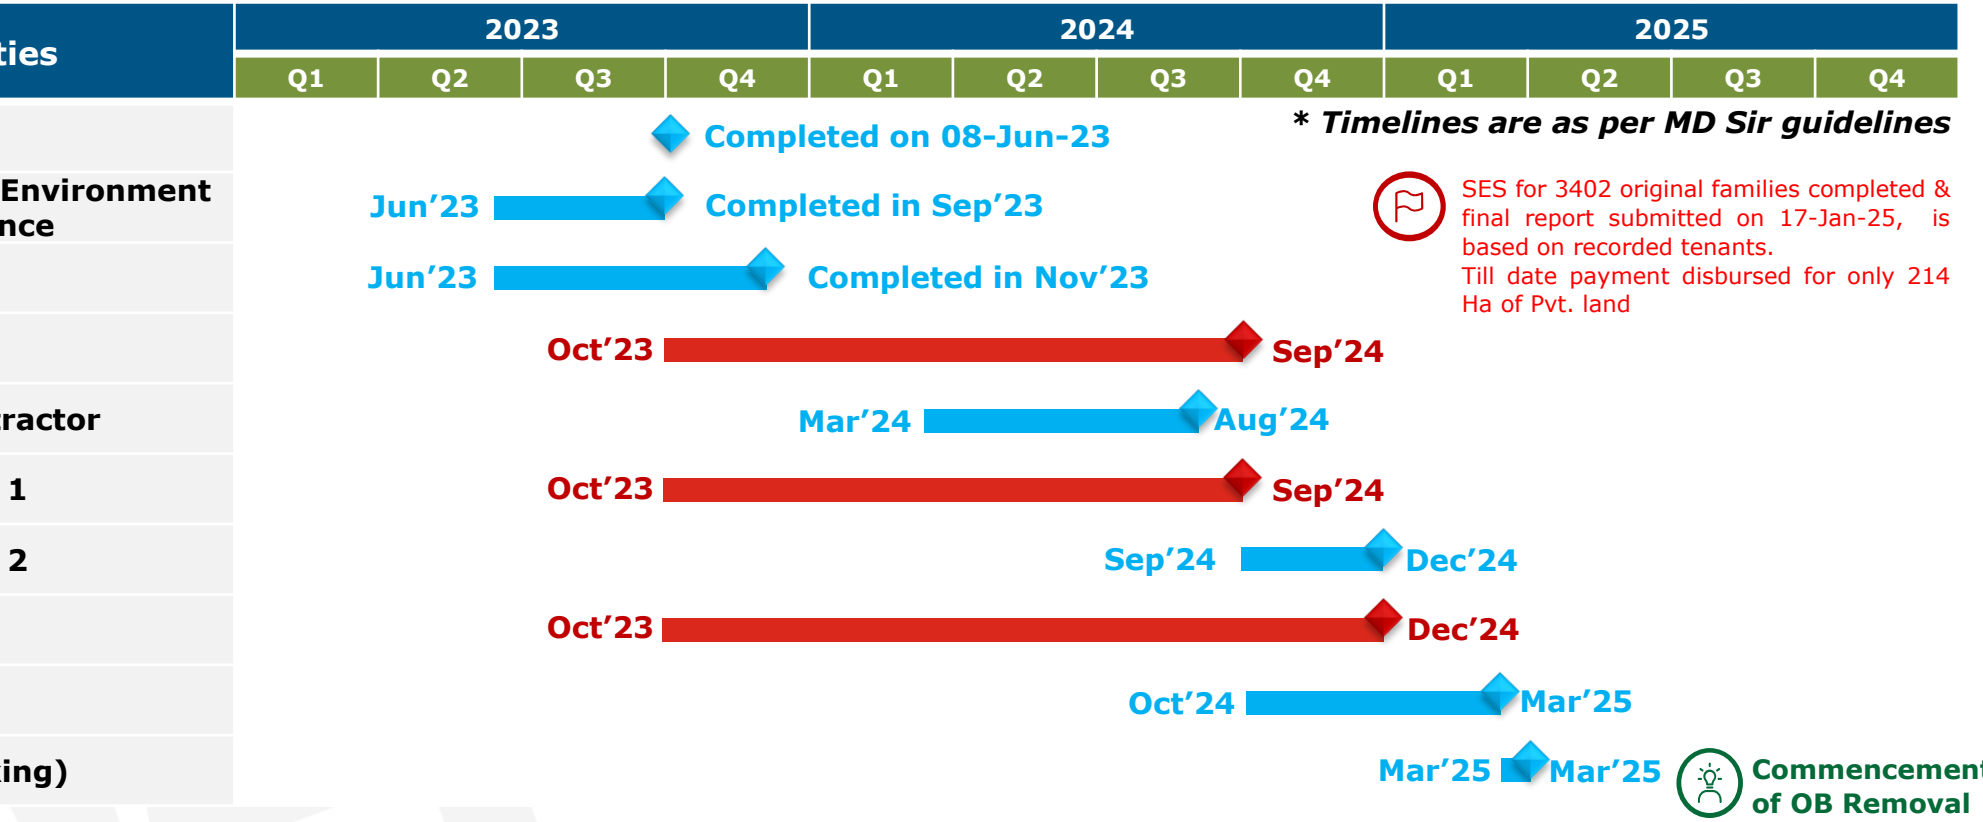


Summary of Key Issues, Mitigation & Responsibility

Issues	Mitigation	Criticality	Action by	Due Date
SES for 3402 original families completed & final report submitted on 17-Jan-25, is based on recorded tenants. It created issue in RPDAC meeting. **Critical**	BNB needs to be prepared solid PAF and PDF data for R&R colony including extended families before RPDAC meeting.	High	BNB	30-Nov-26
Case file for 240 Ha Pvt land acquisition to be prepared. Till date 214 Ha been finalized & validated, As every month price changing, files have to be revised. **Potential Delay**	BNB has to prepare and validate case files for 199 Ha(5yr Mining) of land at the earliest with no of beneficiaries to plan payment process.	High	BNB	30-Sep-26
Land for R&R colony & Gauchar land to be finalized before RPDAC and EC.	Final Requirement of R&R Colony land before RPDAC meeting and Gochar land before EDS submission for FC	High	BNB	30-Sep-26

High Level Schedule – Baitarni West

Efficiency parameters comparison of Coal Block Development and Production Agreement (CMDPA) with MD Sir Plan and Actual/Forecast status

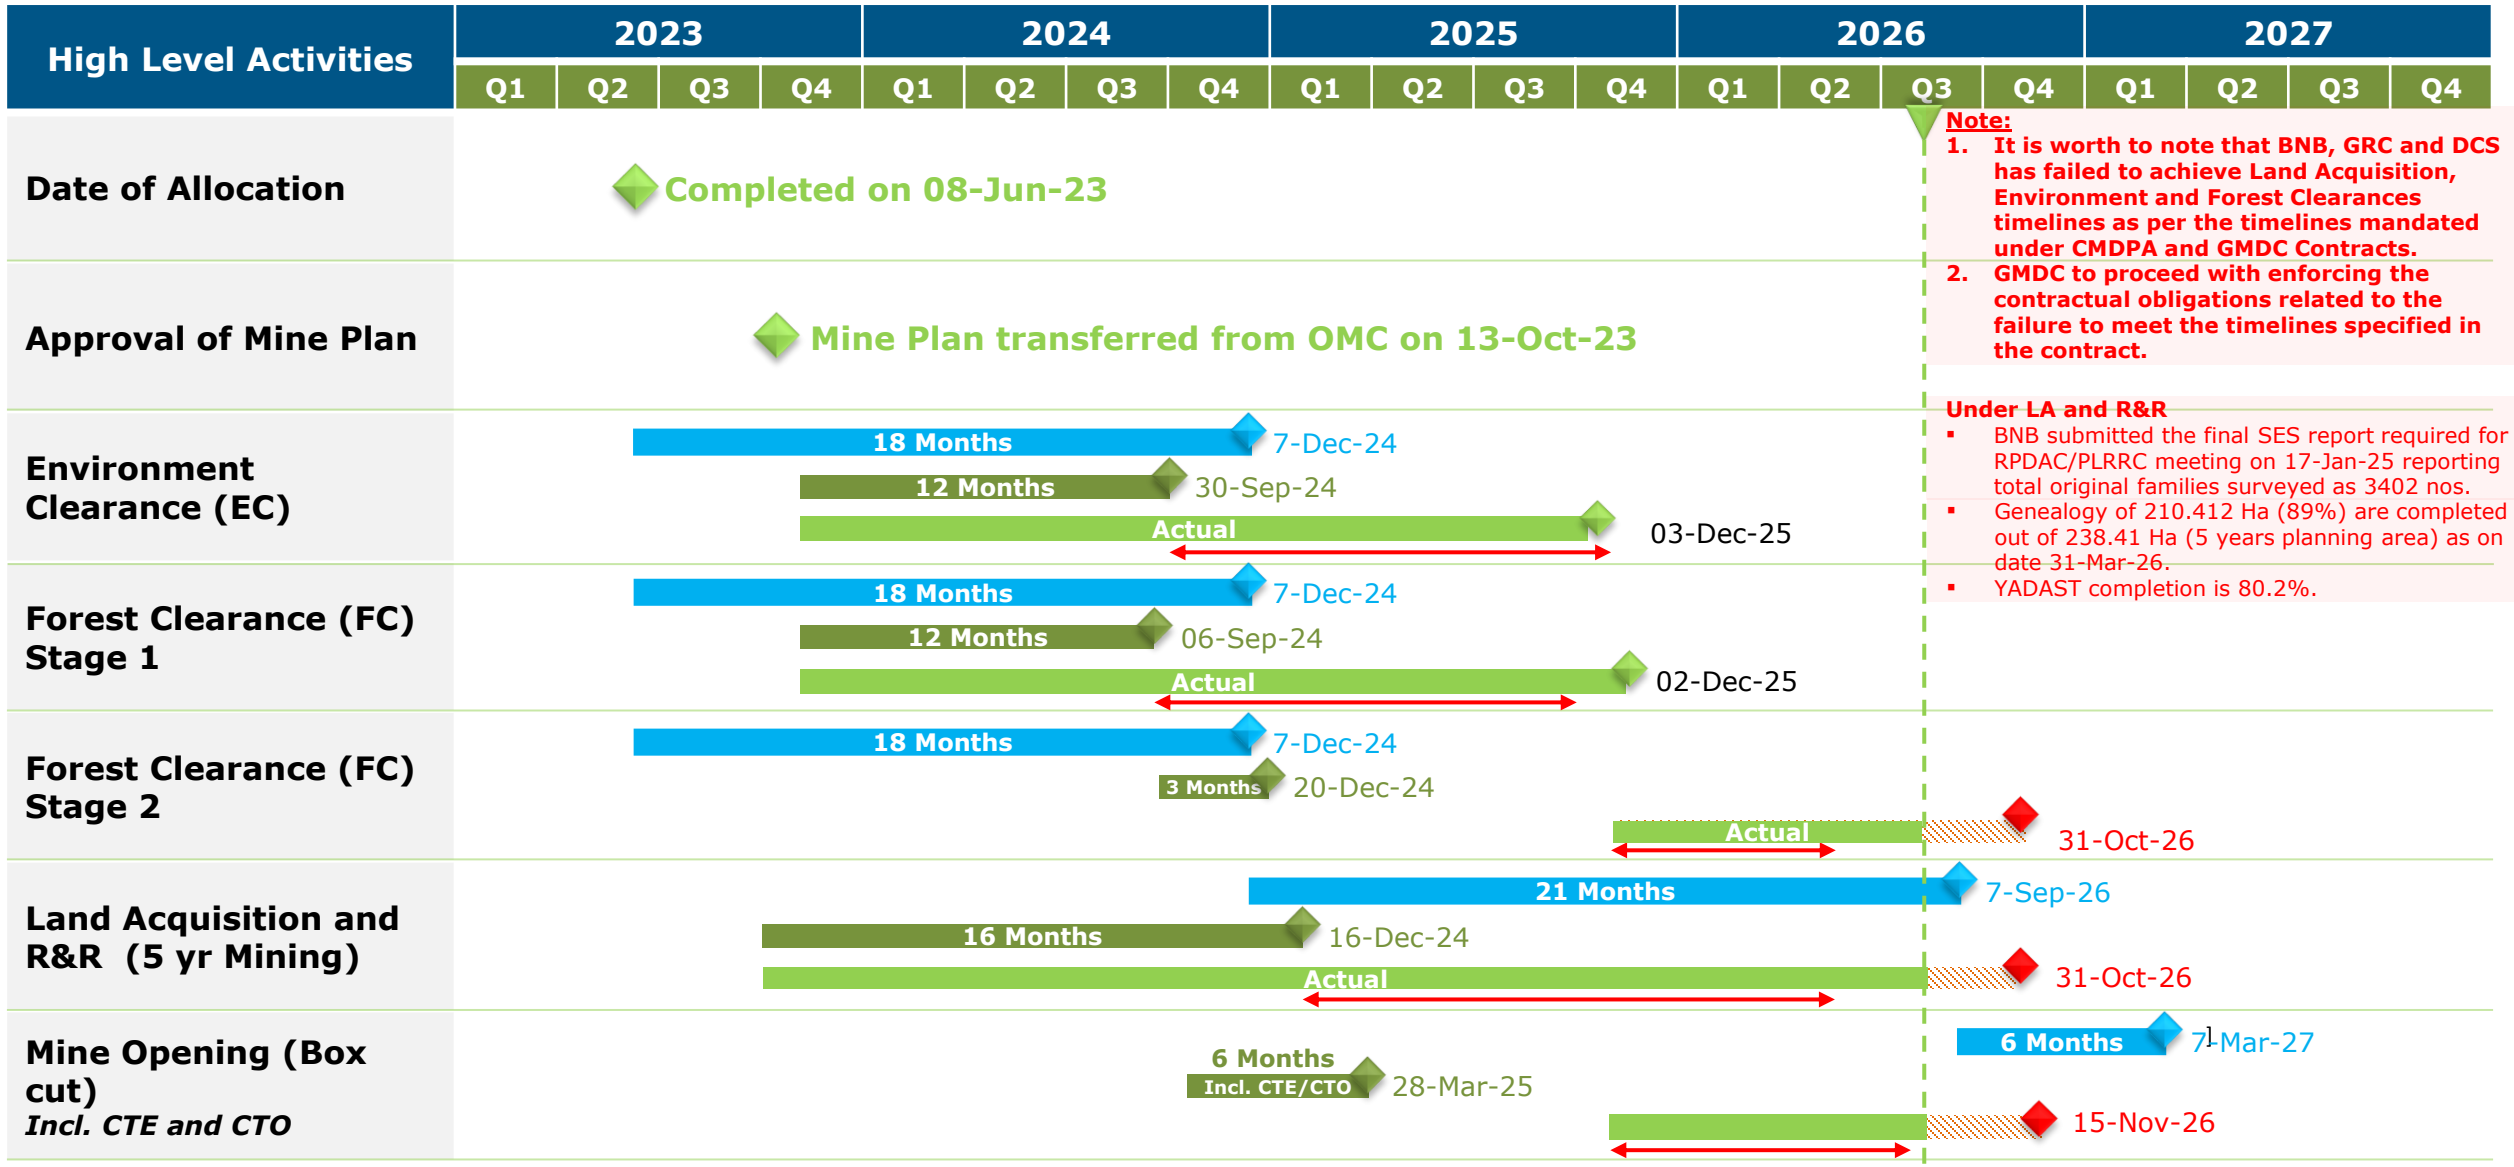

© 2026 Deloitte Touche Tohmatsu India LLP

Payment of the Upfront Amount

Baitarni West

The upfront amount shall be payable in four equal installments [of 25% (twenty five percent each)]

Sr. No.	Installment	Upfront Amount in four equal installments of 25%	Payable To	Fully Explored Mines (Other than Schedule II)	Upfront Amount (INR)	Due Date as per CMDPA Timeline	Actual Payment Date	Remarks
1	First	25%	Nominated Authority	**Within 40 (forty) Business Days** of **execution of the Agreement i.e. 29-Mar-23**	**1,250,000,000**	**08-May-23**	**02-May-23**	**Payment Done**
2	Second	25%	State Government	**Within 15 (fifteen Business Days** of **execution of the Mining Lease or order by the Central Government** under Section 11 (1) of the CBA Act, 1957 i.e. 13-Oct-23	**1,250,000,000**	**28-Oct-23**	**04-Jan-24**	**Payment Done** *Delay was on account of State Government*
3	Third	25%	State Government	**Within 15 (fifteen Business Days** of **grant of the Coal Mine opening permission i.e. 7-Mar-27**	**1,250,000,000**	**22-Mar-27**	**-**	**-**
4	Fourth	25%	State Government	**Within 15 (fifteen Business Days** of **date of commencement of coal production**	**1,250,000,000**	**TBU**	**-**	**-**

© 2026 Deloitte Touche Tohmatsu India LLP


TBU - To be updated

Payment of the Performance Security

Baitarni West

In case of delay in achievement of the Efficiency Parameters, there will be appropriation of Performance Security

Activity	% of Performance Security to be appropriated	Tentative Amount* (INR Cr)
Approval of Mining Plan	10%	111
FC and EC	10%	111
Land Acquisition and Possession of Land	25%	276
Mine Opening Permission	25%	276



Approval received, Mine Plan transferred from OMC to GMDC on 13-Oct-2023

FC and EC is on the critical path and as per CMDPA Milestones it was expected to be completed on 08-Dec-24

8-Dec-24

03-Dec-25

Note: GRC & DCS has failed to achieve Environment and Forest Clearances timelines as per the timelines mandated in CMDPA Agreement.

Note: BNB has failed to achieve agreed-upon project milestones, as stipulated in the contract.

8-Sep-26

Note:
It is to be notified to the GMDC of the imposition of LD, in accordance with the provisions specified under the contract, to address the inconvenience, financial impact, and disruption caused by the delays of BNB, GRC and DCS.

8-Mar-27

© 2026 Deloitte Touche Tohmatsu India LLP

* Amount will vary based on the Performance Security of the year

Detailed Schedule Activities Mine Plan & Turnkey Contractor Onboarding

Baitarni West

Delayed In control Completed

Mining Plan					
S. No.	**Milestone**	**Planned Finish**	**Exp/Act Finish**	**Status**	**Remarks**
1	Commencement of Work	24-Jul-23	1-Aug-23 *(Completed)*	●	**Completed.** ToR documents transferred by OMC on 13-Oct-23. ToR transferred to GMDC on 06-Nov-23.
2	Submission of Project Assumptions relating to Geology, Mine Design and Mine Planning Parameters and other considerations to GMDC management	15-Aug-23	15-Aug-23 *(Completed)*	●	
3	Submission of Mine Plans to MoC	19-Sep-23	19-Sep-23 *(Completed)*	●	
4	Approval of Mine Plan from MoC	29-Nov-23	06-Nov-23 *(Completed)*	●	

Onboarding of Turnkey Contractor for Coal and OB					
S. No.	**Milestone**	**Planned Finish**	**Exp/Act Finish**	**Status**	**Remarks**
1	Preparation and Floating of RFP	5-Apr-24	13-Jan-25 *(Completed)*	●	• The tender has been floated on 13-Jan-25 and Final date for bid submission is 07-May-25. • Pre-bid meeting held on 17-Feb-25 at GMDC Office, Ahmedabad & MS office. Total 14 bidders participated. • LOI & Contract Award completed
2	Pre-bid meeting and response to clarifications	29-Apr-24	14-Feb-25 *(Completed)*	●	
3	Submission of bids	20-May-24	9-Jun-25 (Completed)	●	
4	Evaluation of technical bids	4-Jun-24	10-July-25 (Completed)	●	
5	Evaluation of financial bids	27-Jun-24	05-Aug-25 (Completed)	●	
6	Obtaining approval from competent authority and award of work	11-Jul-24	13-Nov-25 (Completed)	●	
7	Performance security deposit	25-Jul-24	30-Nov-25	●	
8	Site handover ⟷ Ongoing	8-Aug-24	10-Aug-26	●	
9	Signing of Mining contract	8-Sep-24	17-Sep-26	●	
10	Mobilization of resources of Bidder part	30-Aug-24	30-Aug-26	●	

Detailed Schedule Activities EC

Baitarni West

Delayed In control Completed

Environment Clearance					
S. No.	**Milestone**	**Planned Finish**	**Exp/Act Finish**	**Status**	**Remarks**
1	Start Date for Environmental Clearance Works	6-Oct-23	6-Oct-23 *(Completed)*	●	1. PH conducted on 24-Sep-24. 2. With reference to the meeting dtd. 13-Dec-24, all the agencies to work collectively towards the completion and finalization of EIA-EMP report. 3. GRC has submitted the final EIA-EMP report on 23-Jan-25. 4. EDS received on 03-Feb-25. Responses submitted on 22-Mar-25. 5. Final technical Presentation before EAC completed on 03-Apr-25. **EAC has returned the proposal in its present form as per the MOM of 23rd meeting of the EAC published on 11-Apr-25.** **6. GRC shared Final EIA/EMP & Tech. Presentation for review.** **7. R&R plan in report format is completed & provided to GRC.** 8. NOC on elephant corridor is received from PCCF on 25-Aug-25. 9. Final EC submitted on 30-Sep-25. 10. EAC held on 29-Oct-25. Inprinciple approval for EC received on 11-Nov-25. Final EC received on 03-Dec-2025
2	M1 - Grant of ToR by MoEF & CC (Coal Mining)	6-Nov-23	6-Nov-23 *(Completed)*	●	
3	M2 - Baseline Study & Data Collection	12-Dec-23	5-Jan-24 *(Completed)*	●	
4	M3 - Preparation of Additional Studies & Reports in compliance of ToR	26-Jun-24	14-Jul-25 *(Completed)*	●	
5	M4 - Draft EIA submission to SPCB for further conduction of Public Hearing	9-Feb-24	12-Feb-24 *(Completed)*	●	
6	M5 - Support in Public Hearing/ Public Hearing Presentation	11-Apr-24	24-Sep-24 *(Completed)*	●	
7	M6 - Final EIA & EMP report submission to MoEF&CC	5-Jun-24	30-Sep-25 *(Completed)*	●	
8	M7 - Final Technical Presentation in front of EAC (Coal Mining)	12-Aug-24	29-Oct-25 *(Completed)*	●	
9	M8 - Grant of EC by MoEF & CC (Coal Mining)	30-Sep-24	03-Dec-25 *(Completed)*	●	

© 2026 Deloitte Touche Tohmatsu India LLP

Detailed Schedule Activities FC

Baitarni West


Delayed In control Completed

Forest Clearance					
S. No.	**Milestone**	**Planned Finish**	**Exp/Act Finish**	**Status**	**Remarks**
1	Start Date for Forest Clearance Works	6-Oct-23	6-Oct-23 *(Completed)*	●	1. Final FDP file submitted on 21-Mar-25 excluding Wild-Life Management Plan. 2. Letter sent to DG Forest, MOEF&CC, on 09-Jun-25 requesting expedition of FC Grant. 3. SSWLCP meeting with PCCF conducted on 29-Jul-25. 4. DFO sent Revised SSWCP to RCCF on 25-Aug-2025. 5. NOC on elephant corridor is received from PCCF on 25-Aug-25. 6. FAC held on 27-Oct-25. Grant of inprinciple approval is recommended in the released MoM 7. FC stage-01 granted on 02-Dec-2025. 8. All the demands has been received and payment done. 9. 11 Schemes out of 12 approved on 10-Apr-26 from RCCF, Angul. 10. PF notification of CA land done on 11-Jun-2026. 11. SMC plan approved on 30-Jun-26. 12. Stage-01 compliance submitted to DFO on 04-Jul-26. 13. DFO forwarded to PCCF Nodal on 19-Jul-26. **14. RCCF forwarded the file to PCCF Nodal on 24-Aug-26** **15.PCCF forwarded the file to MoEF on 8-Oct-26** **16. NOC for Nala Diversion expected by 30-Oct-26.**
2	M1 - Project & Forest Area mapped, Land Details	24-Nov-23	30-Nov-23 *(Completed)*	●	
3	M2 – DGPS by CMPDIL for Mining lease hold area	11-Dec-23	12-Jan-24 *(Completed)*	●	
4	M3 - Compensatory Afforestation (CA) Land Process	28-Mar-24	12-Apr-24 *(Completed)*	●	
5	M4 - Activities for Tree Enumeration	10-Jan-24	11-Jun-24 *(Completed)*	●	
6	M5 - Online filing of FDP & comply of EDS	9-Apr-24	10-Jul-24 *(Completed)*	●	
7	M6 - Activities for approval under (FRA) 2006 ← Ongoing →	28-Nov-24	23-Sep-25	●	
8	M7 - NOC from Gram Panchayat, Archaeological Dept., and Collector	13-Nov-24	8-Sep-25	●	
9	M8 - Details regarding land and R&R required for submission of FC app.	10-Jul-24	12-Feb-25	●	
10	M9 - Processing by the Nodal Officer of the Processing Authority	15-Mar-24	9-Aug-24	●	
11	M10 - Processing of the proposal by the DFOs/ DCs	30-Apr-24	25-Oct-24	●	
12	M11 - Processing of the proposal by the CF/CCF	28-May-24	7-Dec-24	●	
13	M12 - Processing of the proposal by the Nodal Officer	24-Jul-24	25-Sep-25	●	
14	M13 - Processing of the proposal by the State Govt. & Issue of FC Stg-1	6-Sep-24	10-Oct-25	●	
15	M14 - SSWLP Formulation and submission	18-Sep-24	25-Sep-25	●	
16	M15- FAC Presentation & Stage-01 approval	30-Sep-24	02-Dec-25	●	
17	M15 - Payment for NPV, CA Land etc.	3-Oct-24	15-Jun-26	●	
18	M16 - Compliance activities of Stage-I conditions ← Ongoing →	25-Oct-24	15-Aug-26	●	
19	M17 - Issuance of Stage-II FC	20-Dec-24	31-Oct-26	●	


Detailed Schedule Activities – Land Acquisition and R&R

Land

Government Land(Ha)

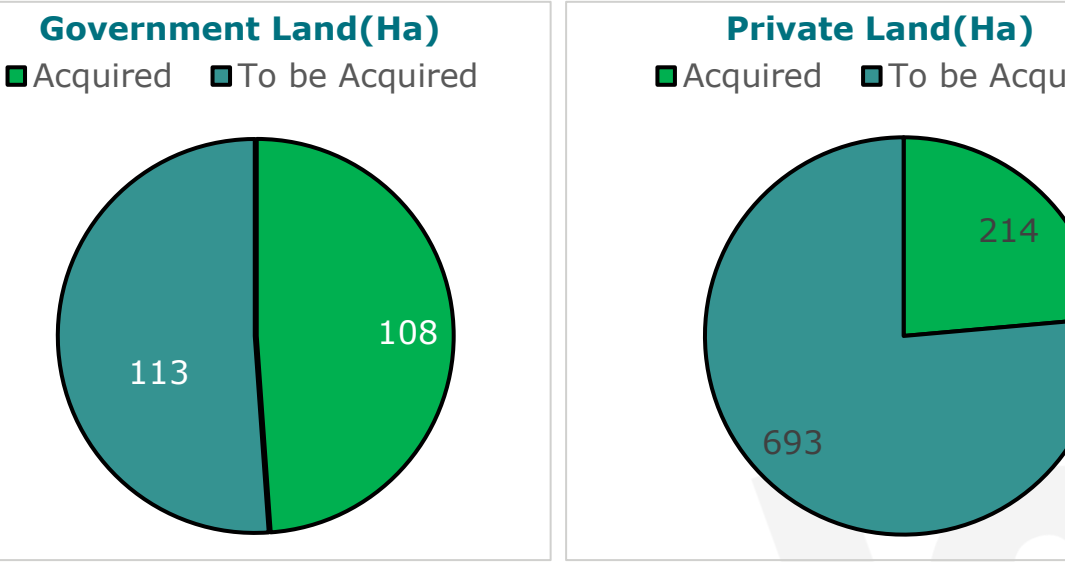


Private Land(Ha)

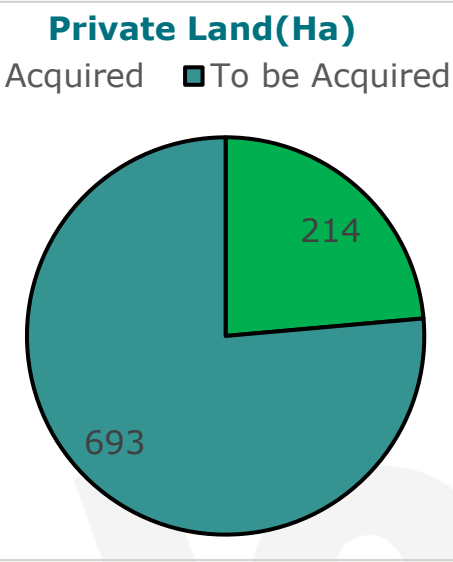

PAP

Project Impact

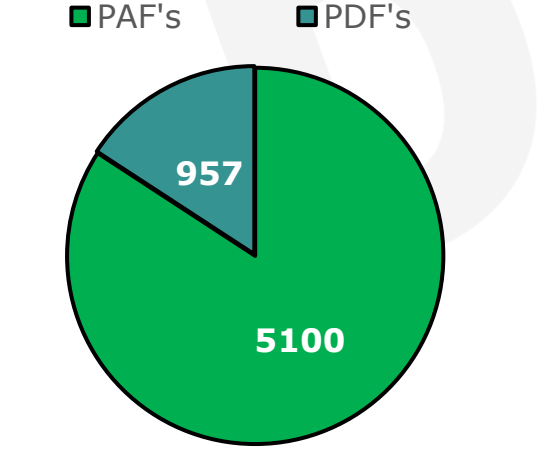

PAF's Detail

- Cash in Liew of Land
- Employment in Lieu of Land

Land Acquisition

Forest Land =64 Ha	Govt. Land = 221 Ha	Private Land = 907 Ha

S. No.	Milestone	Planned Finish	Exp/Act Finish
1	M1 - Preparation of Land documents for filling of land acquisition under CBA	13-Oct-23	13-Oct-23 *(Completed)*
2	M2 - Notification in Official Gazette under Section 4(1)	13-Oct-23	13-Oct-23 *(Completed)*
3	M3 - Notification u/s 7(1) of CBA (A&D) Act, 1957	13-Oct-23	13-Oct-23 *(Completed)*
4	M4 - Socio Economic Survey	22-May-24	17-Jan-25 *(Completed)*
5	M5 - Section 8 hearing and disposal of objections	13-Jun-24	4-Jun-25 *Completed*
6	M6 - Notification u/s 9(1) of CBA (A&D) Act, 1957-Declaration of Acquisition.	13-Oct-23	*Completed*
7	M7 - Notification u/s 11(1) of CBA (A&D) Act, 1957	13-Oct-23	*Completed*

Resettlement & Rehabilitation

S. No.	Milestone	Planned Finish	Exp/Act Finish
1	M8 - Determine and Finalize Compensation u/s 13 and 14 of CBA (A&D) Act, 1957	28-Aug-24	19-May-26
2	M9 - R&R Scheme and Compensation Scheme award	16-Jul-24	6-Nov-25
3	M10 - Compensation Payment (5-year Mining) Ongoing	28-Aug-24	**30-Nov-26**
4	M11 - Transfer & physical possession of Private Land (for at least 5 years of operatn)	5-Dec-24	26-Mar-26
5	M12 - Transfer & physical possession of balance Private Land	16-Dec-24	7-Apr-26

SES for 3402 original families completed & final report submitted on 17-Jan-25, is based on **recorded tenants**.

Actions to be taken within next 15 days

Baitarni West

Delayed | In control | Completed

Particulars	Contractor	Status as on date	Criticality	Action Plan
Land Acquisition and R&R	BNB	▪ SES for 3402 original families completed & final report submitted on 17-Jan-25, is based on recorded tenants. ▪ BNB has submitted the Final SES report as per Recorded Tenant numbers which may have impact on RPDAC meeting. ▪ Payment disbursement for ~152 Ha. of private land has been acquired as on 15-Apr-26. ▪ Payment for 108.13 Govt land has been completed as on 30-Mar-26 (5-year planned Govt. Land done). Letter shared by GMDC for physical possession on 04-Apr-26 ▪ GMDC shared letter to DC, Angul requesting to finalize date for RPDAC on 24-Feb-26. ▪ RPDAC meeting held on 07-Oct-26.		▪ BNB to focus on the completion of Genealogy & YADAST for the families falling under 3- and 5-years mining area plan. ▪ BNB to complete Genealogy of PDFs in all respect at the earliest before conduction of RPDAC Meeting. ▪ GMDC should focus on land acquisition for Railway Siding as per DPR. ▪ BNB must prepare and validate case files for 199 Ha of land at the earliest for acquisition & possession. ▪ **BNB should focus on land acquisition of the approach road connecting Chhendipada-Jharpada road to Mine Lease Boundary.** ▪ **Tree cutting from Govt. Land and acquired Pvt. Land to be done by 30-Sep-26.**
EC	GRC	▪ PH conducted on 24-Sep-24 & MS, SPCB BBSR sent proceeding of PH to MoEF RO Bhubaneswar & HO, New Delhi for necessary action. ▪ Proceeding of PH incorporated in Final EIA & EMP report and finalized in all respect. GRC has submitted Final EIA & EMP report to MoEF & CC on 23-Jan-25. GRC submitted Final Technical Presentation to GMDC for review on 11-Feb-25. ▪ EDS received on 03-Feb-25. Responses submitted on 22-Mar-25. ▪ Final presentation done in 23rd EAC meeting dated 03-Apr-25. ▪ EAC has returned the proposal in its present form as per the MOM of 23rd meeting of the EAC published on 11-Apr-25. ▪ Final EC application submitted on 30-Sep-2025 and included in EAC agenda of Oct month. ▪ EAC held on 29-Oct-2025. ▪ **EC Granted on 03-Dec-2025.**		▪ GRC has to comply if any condition or studies recommended in the EC condition and follow up with DCS for FC Stage-02 compliances.

Actions to be taken within next 15 days

Baitarni West

Delayed In control Completed

Particulars	Contractor	Status as on date	Criticality	Action Plan
FC	▪ GRC/ DCS	▪ FAC held on 27-Oct-25. ▪ FC-Stage-01 granted on 02-Dec-25 ▪ Letter received from Tehsildar Baipariguda on 20-Jan-26 for payment of premium of CA land cost for mutation. ▪ CA land mutation completed, and ROR received. ▪ Letter for CA land PF notification submitted to DFO Jeypore on 17-Feb-26. ▪ Stage-01 compliance is in progress. Submission of 11 schemes along with Avifauna Scheme to DFO completed on 30-Mar-26 as part of compliance to FC-I conditions. ▪ Letter to issue NoC along with Project report for Nallah Diversion submitted to Chief Engineer, Water Resources Department on 06-Mar-26. ▪ DPR for Nala Diversion submitted on 12-Mar-26. Chief Engineer in Charge, Water Resource Dept. sent letter on 24-Mar-26 to Chief Engineer, Samal Basin to conduct a joint filed survey along with Megagift and Minor Irrigation Field Officers. ▪ *17-Apr-26 Joint visit completed, and they have submitted their report to Chief Engineer in Charge, Water Resource Dept on 29-Apr-26.* ▪ *PF notification for CA land completed on 11-Jun-26.* ▪ *SMC Scheme approved by DFO Angul on 30-Jun-26.* ▪ Stage-01 compliance submitted to DFO on 04-Jul-26. ▪ DFO Forwarded the file to RCCF & PCCF on 19-Jul-26. ▪ **RCCF forwarded the Stage-01 compliance on 24-Aug-26.** ▪ **PCCF instructed to DFO to raise demand for additional CA land cost as per approved 2026-27 onetime cost norm on 08-Sep-26.** ▪ **DFO raised the demand to GMDC on 10-Sep-26.** ▪ **GMDC paid the amount on 17-Sep-26, but money refunded.** ▪ **Again, GMDC paid on 22-Sep-26 and submitted a letter to DFO on 23-Sep-26.** ▪ **DFO processed the file and submitted to PCCF on 25-Sep-26.** ▪ **PCCF Nodal forwarded the file to MoEF on 8-Oct-26 for further processing.**		▪ Human-Elephant conflict study and FRA certification to be completed at the earliest time frame. ▪ GRC to obtain NOC under FRA 1980 through DCS as a mandatory requisite for FC-II clearance approval by 05-Oct-26 ▪ **DCS should follow up with PCCF for movement of FC-I compliance file to MOEF at the earliest.** ▪ **FC-I compliance file sent to MOEF on 8-Oct-26**

Actions to be taken within next 15 days

Baitarni West

Delayed In control Completed


Particulars	Contractor	Status as on date	Criticality	Action Plan
Logistics	IPRCL	▪ DPR submitted to GMDC for review on 25-Mar-25. Presentation on DPR completed on 15-Mar-25 at RCO, BBSR. ▪ DPR submitted on 17-Jun-25 to ECoR. ▪ Observations received on 29-Jul-25, reply to DRM Sambalpur on 19-Aug-25. ▪ Observations received again on 20-Sep-25 and Compliance sent on 30-Sep-25. ▪ Letter received from Divisional Railway Manager on 30-Dec-25 to provide NOC. ▪ NOC given to Divisional Railway Manager to proceed further for DPR approval on 25-Feb-2026 ▪ Compliance on Observations of Railway on ESPS completed on 26-Mar-26.		▪ **Land identification at Jharpada siding for coal Stock.** ▪ **DPR compliance & Follow up for DPR approval.**
Mine Opening Permissions	GMDC	▪ CTE Applied on 02-Jan-26. Payment & final query response submitted on 12-Feb-26. ▪ Presentation in front of Committee completed on 18-Mar-26. ▪ CTE approved on 29-Apr-26. ▪ Escrow agreement completed. ▪ CTO applied on 08-Jul-26 and queries received 15-Jul-26. ▪ **LIN generated on 18-Aug-26** ▪ **Comply of the queries submitted to OSPCB and payment done 12-Aug-26**		▪ **Liasioning with SPCB to get observation on CTO except FC-II.**

High Level Schedule of IPRCL

Baitarni West

Consultancy Services for Feasibility Study on development of dedicated Rail Terminal near BW coal mine taking off nearest station of MCRL corridor

Delay | Key Milestones | Plan | Actual | Forecast

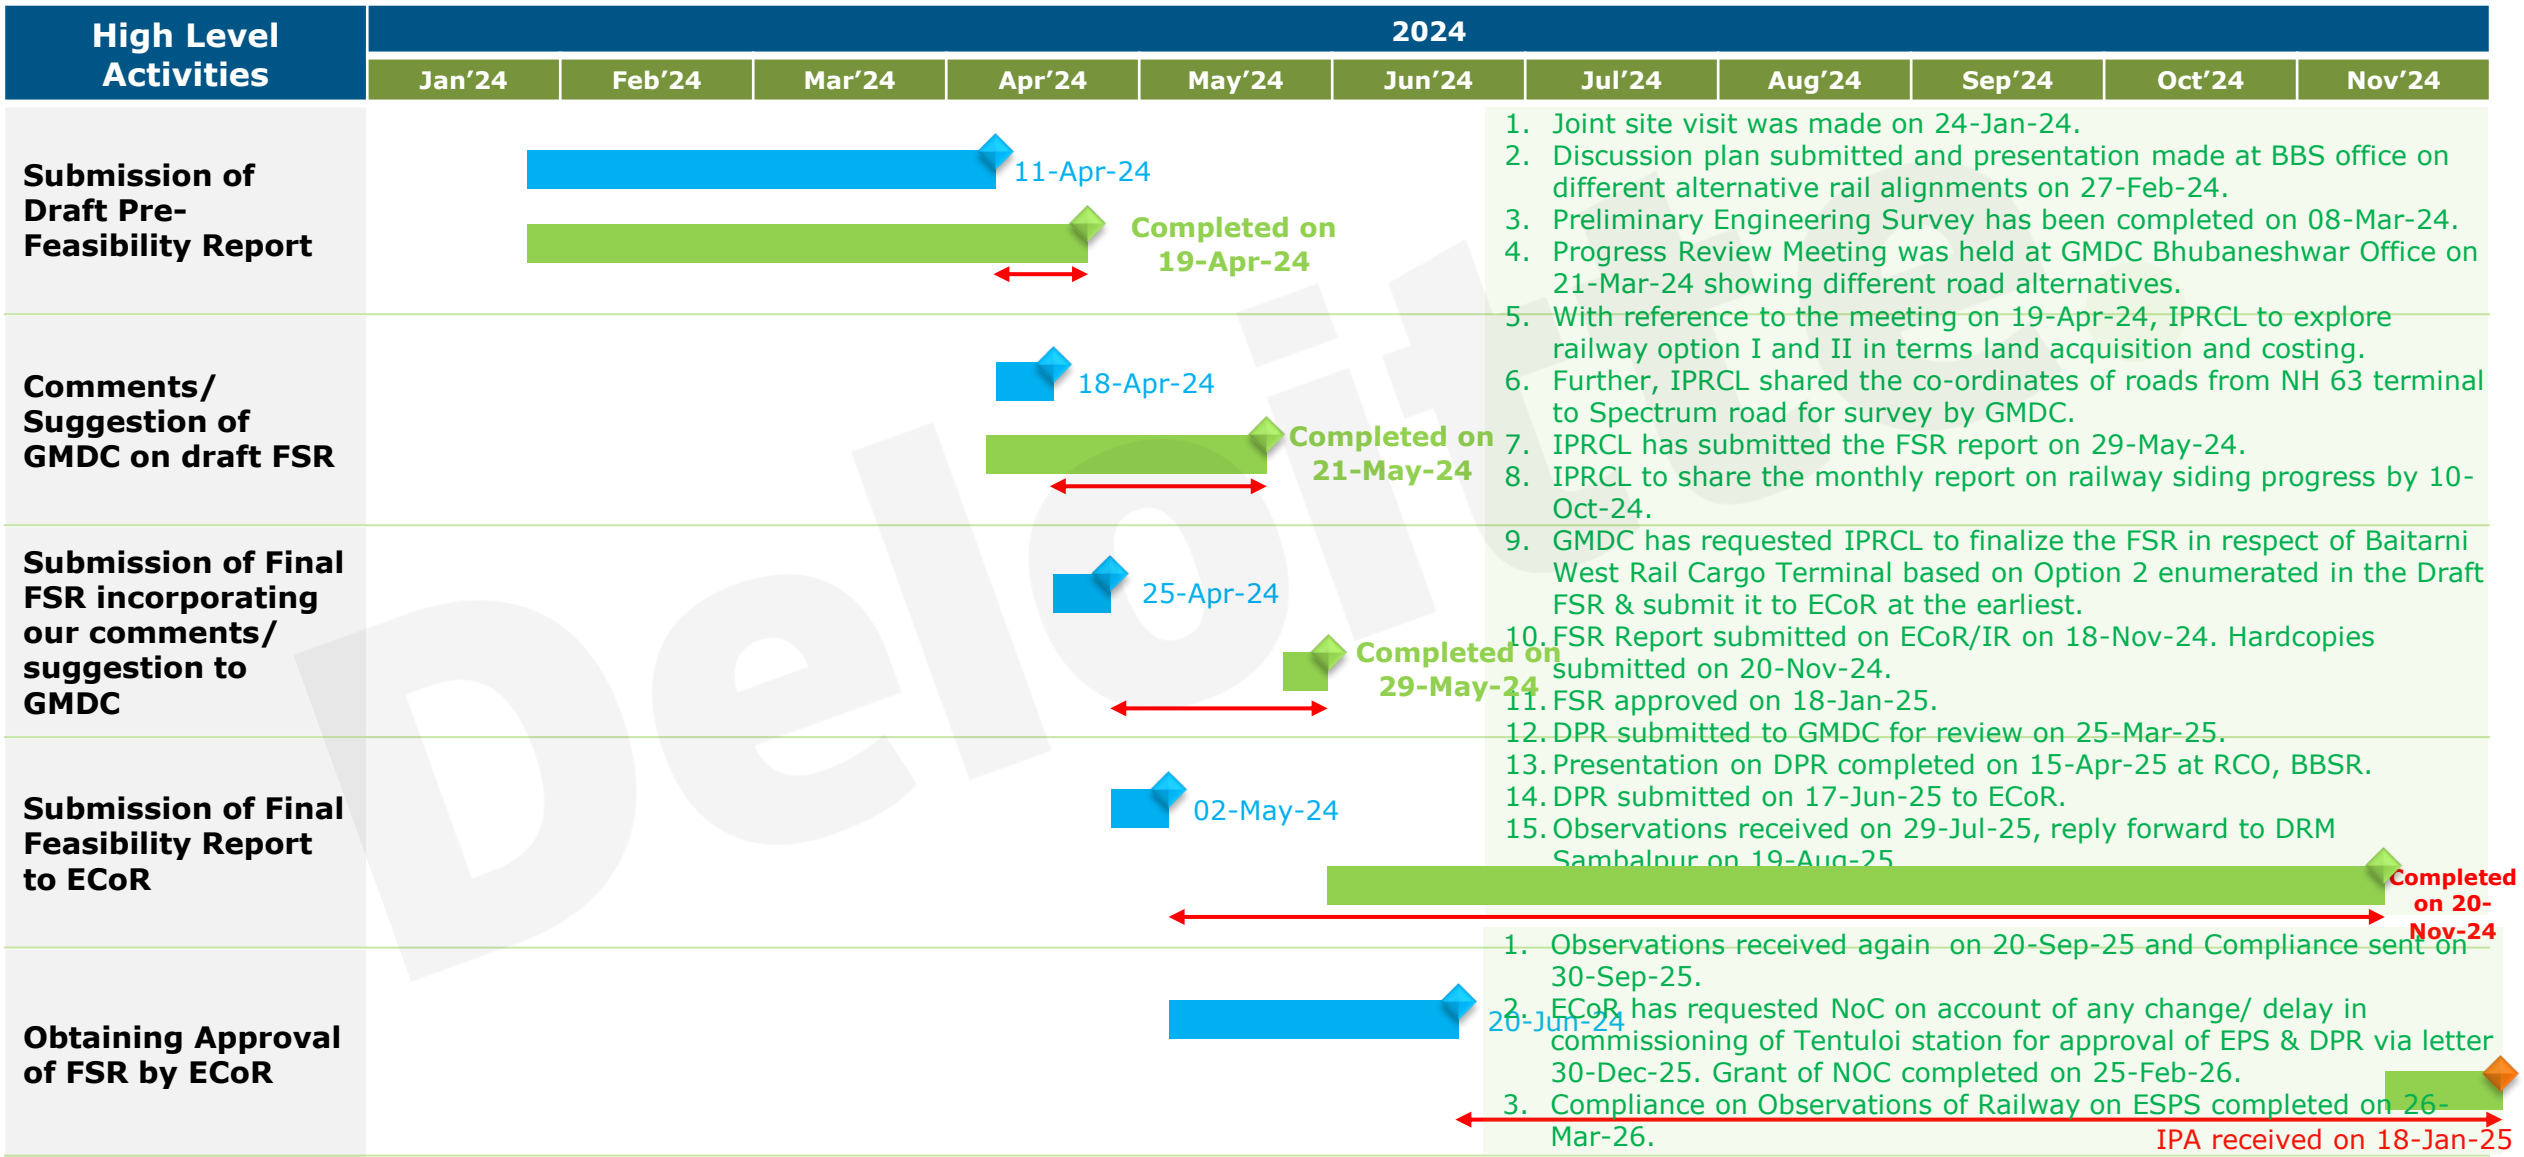

1. Joint site visit was made on 24-Jan-24.
2. Discussion plan submitted and presentation made at BBS office on different alternative rail alignments on 27-Feb-24.
3. Preliminary Engineering Survey has been completed on 08-Mar-24.
4. Progress Review Meeting was held at GMDC Bhubaneshwar Office on 21-Mar-24 showing different road alternatives.
5. With reference to the meeting on 19-Apr-24, IPRCL to explore railway option I and II in terms land acquisition and costing.
6. Further, IPRCL shared the co-ordinates of roads from NH 63 terminal to Spectrum road for survey by GMDC.
7. IPRCL has submitted the FSR report on 29-May-24.
8. IPRCL to share the monthly report on railway siding progress by 10-Oct-24.
9. GMDC has requested IPRCL to finalize the FSR in respect of Baitarni West Rail Cargo Terminal based on Option 2 enumerated in the Draft FSR & submit it to ECoR at the earliest.
10. FSR Report submitted on ECoR/IR on 18-Nov-24. Hardcopies submitted on 20-Nov-24.
11. FSR approved on 18-Jan-25.
12. DPR submitted to GMDC for review on 25-Mar-25.
13. Presentation on DPR completed on 15-Apr-25 at RCO, BBSR.
14. DPR submitted on 17-Jun-25 to ECoR.
15. Observations received on 29-Jul-25, reply forward to DRM Sambalpur on 19-Aug-25

1. Observations received again on 20-Sep-25 and Compliance sent on 30-Sep-25.
2. ECoR has requested NoC on account of any change/ delay in commissioning of Tentuloi station for approval of EPS & DPR via letter 30-Dec-25. Grant of NOC completed on 25-Feb-26.
3. Compliance on Observations of Railway on ESPS completed on 26-Mar-26.

© 2026 Deloitte Touche Tohmatsu India LLP



Deloitte.

Deloitte refers to one or more of Deloitte Touche Tohmatsu Limited, a UK private company limited by guarantee ("DTTL"), its network of member firms, and their related entities. DTTL and each of its member firms are legally separate and independent entities. DTTL (also referred to as "Deloitte Global") does not provide services to clients. Please see www.deloitte.com/about for a more detailed description of DTTL and its member firms.

This material has been prepared by Deloitte Touche Tohmatsu India LLP ("DTTILLP"), a member of Deloitte Touche Tohmatsu Limited, on a specific request from you and contains proprietary and confidential information. This material may contain information sourced from publicly available information or other third party sources. DTTILLP does not independently verify any such sources and is not responsible for any loss whatsoever caused due to reliance placed on information sourced from such sources. The information contained in this material is intended solely for you. Any disclosure, copying or further distribution of this material or its contents is strictly prohibited.

Nothing in this material creates any contractual relationship between DTTILLP and you. Any mutually binding legal obligations or rights may only be created between you and DTTILLP upon execution of a legally binding contract. By using this material and any information contained in it, the user accepts this entire notice and terms of use.

©2024 Deloitte Touche Tohmatsu India LLP. Member of Deloitte Touche Tohmatsu Limited
